




Kids Kingdom II Update

Kids Kingdom Update as of April, 12, 2012:
Construction and final site work has resumed.
Our best estimate is that work will be completed around April 30th.

- Playground was substantially completed in Fall/Winter 2011/12
- Most permanent features have been installed with a few exceptions that include; toddler swings, cargo netting, blacktop walkways, safety surfacing, benches and landscaping.
- Volunteer opportunity exists for those community members willing to help with landscaping the playground area on Sunday April 29th. For more information contact Deirdra Wallin at Deirdra114@yahoo.com for details.
- Ribbon cutting ceremony Sunday May 6th at 1 PM

Still River Greenway

B R O O K F I E L D C T

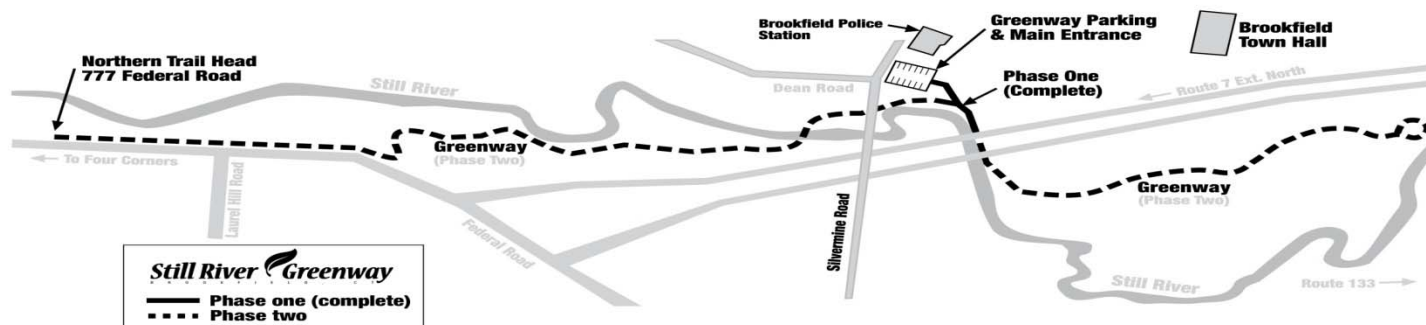

Phase I (Approx. ¼ mile)

- Completed Fall of 2011
- New paved trail provides parking (adjacent to the Police Department) and approx. ¼ mile of paved trail that ties into existing earth trail headed south for a total distance of about 1 mile.

Phase II (Approx. 2 miles)

- This portion of the project is currently in the Final design stage.
- Will require a local match of 20% of the project.
 - Will require Local, State and Federal wetland permitting.
- Possibility of breaking ground on the balance of this project in 12 – 16 months

Proposed trail uses include: *Hiking, walking, jogging, bicycling, rollerblading / skateboarding, cross-country skiing, bird watching, motorized wheelchairs (for handicap access only) Open Sunrise to Sunset*
